


Chino Basin Water Conservation District



Brooks Basin Fencing, Phase I

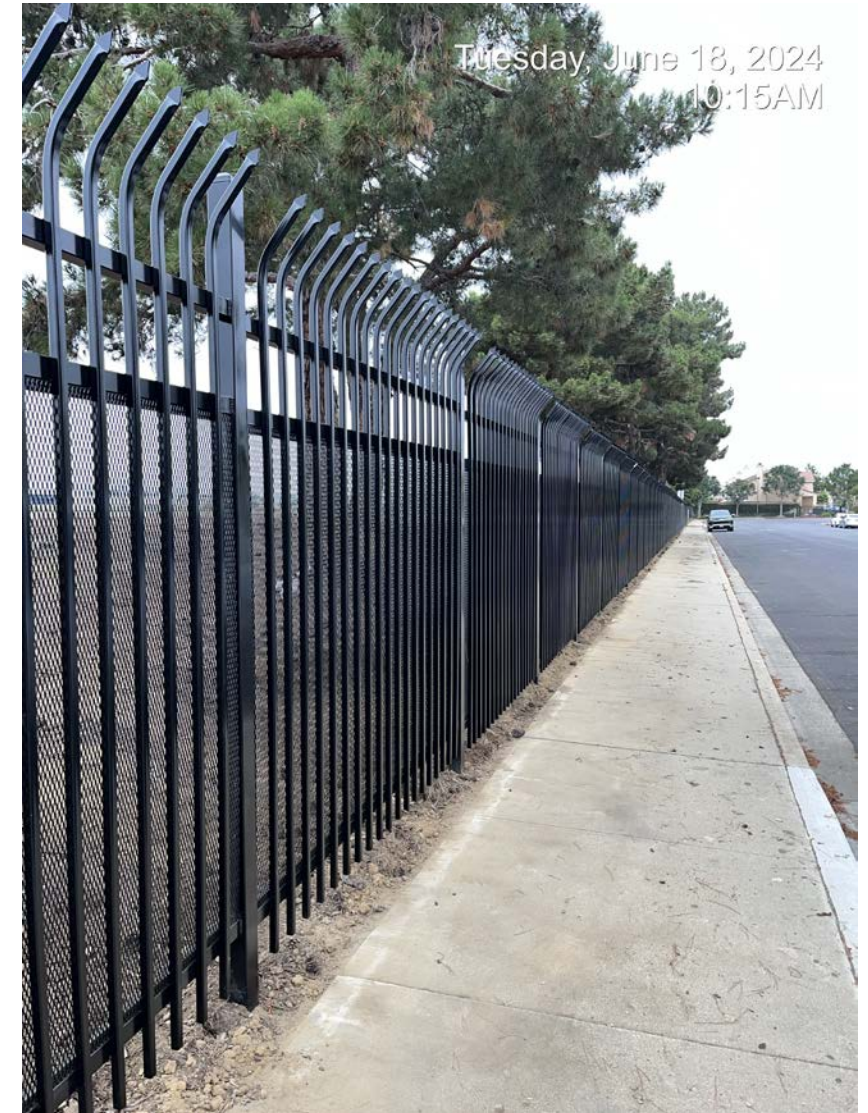

Chino Basin Water Conservation District



Brooks Basin Fencing, Phase I

TIMELINE

- December 11, 2023: CBWCD Board of Directors Award Contract
- Cost: \$298,710.00
- March-August 2024: Materials Fabrication-Demolition of Old Fencing-Construction/Installation
- August 2024: Completion



Brooks Basin Fencing, Phase I

SPECIFICATIONS

- Brooks St. & Silicon Ave.: 1,050 linear feet of iron fencing, 8' tall w/24" top rail pickets, w/expanded metal backing
- Brooks St.: (1) four-foot-wide walk-in gate
- Silicon Ave.: (1) 20' wide double swing gate
- District/Railroad Property Line: 170' welded wire mesh steel w/expanded metal backing. (1) 16' wide double swing gate

Brooks Basin Fencing, Phase I



Holt Blvd.

Holt Blvd



R a m o n a

Appaloosa Way

Atabari Pl

Morgan Cir

Clydesdale Way

Iron Fence

Brooks St

Brooks St.

S i l i c o n

Iron Fence

Gate

Welded Wire Mesh Steel Fence

Phase II

K i m b e r l y

Ramona Ave

State Street

State St

Rd-20010

Gates

Brooks Basin Fencing, Phase I



Silicon Ave.



Brooks Basin Fencing, Phase I



Silicon Ave.



**Iron Fencing w/24"
Steel Pickets**



Brooks Basin Fencing, Phase I



Brooks St.



Brooks Basin Fencing, Phase I



Brooks St.



Brooks Basin Fencing, Phase I



**Welded Wire Mesh
Steel Fencing**



**District/RR property
line**

Brooks Basin Fencing, Phase I



**Welded Wire Mesh
Steel Fencing**

**District/RR property
line**

Brooks Basin Fencing, Phase I



**Welded Wire Mesh
Steel Fencing**

**District/RR property
line**



Brooks Basin Fencing, Phase I



Silicon Ave.- Brooks St.- South Property Line

COMPLETED August 2024



Brooks Basin- Security Retro-fits



'Developers' 7' x 150' wall bordering District property



Brooks Basin- Security Retro-fits



Developers 7' x 150' wall bordering District property



SW Corner-District fence & block wall meet

Brooks Basin- Security Retro-fits



Silicon Ave.- District's New Iron Fencing & Developer's Block Wall



District Property-
Install Plant Material
& Mulch

Remove Developer's
3' x 10' Wall

